





# BATH STREET BUS LANE CONTRAFLOW









Dear Stakeholder.

We hope you are keeping well. In this edition of our newsletter, we are happy to tell you that things are looking up as works have gained back momentum. Southern Water works within our perimeter in the northern end of Bath Street are complete and the works around that area have continued in earnest.

We are aware that some stakeholders experienced certain inconveniences during the night works earlier in September. Though we have responded to each concern, please note that we are keen on hearing from our stakeholders about any further concerns as we strive to carry out the works as safely as possible and with minimal inconvenience.

### **Progress Update**

The works have been Switched to phase 2a, traffic management has been moved from the Southern Corner to the Southern central Reserve Island, we moved pedestrian signals into temporary locations to maintain functionality and removed the redundant CCTV Camera. We are also removing existing asphalt paving and kerbs. We will be carrying out Excavation to prove service locations using Vac Ex, as well as excavation for new pavement construction.

In Phase 1 We have removed unused chambers and covers – and filled with subbase. Laid subbase for pavement, including temporary pavement. Laid ducting for street lighting and signals. Completed the Pavements, and laid temporary Road Surface, which will be completed in Phase 3, we continue to complete the Northern footpath and then switch Traffic to Phase 2 b to enable works to the northern Island.

# **Project Timelines**

The project is in 4 phases.

<u>Phase 1</u> – Road widening on the West side.

Works on footpaths, kerbs, laying of binders, surfaces, and tactile pavers to be completed by mid-August.

<u>Phase 2</u> –Removal and reconstruction of the Central Reservation.

Continuation of Kerb Laying to West side.

Continuation of footpath removal and reinstatement to tarmac surfacing of the footpath and carriageway to continue.

Phase 3 - Road Widening on the East side and works on the Central Section, and BT Chamber Works.

<u>Phase 4</u> – Reinstate Central Reservation islands









## Photos of works in progress









### **Upcoming Works.**

Works on the Central reserve Northern Island are up next, with traffic management set to create single lane traffic in taxi lane and northbound traffic lane. Details of works include;

- Excavating second part of road crossing, install duct and reinstate.
- Remove streetlights and signals, move signals on southern island into barrels to maintain functionality.
- Remove existing signs and bollards, deterrent paving, asphalt paving, and kerbs.
- Excavating to prove service locations using Vac Ex.
- Excavate for new pavement construction.
- Services SGN to undertake installation of new main, connecting to previously installed stub.









## **Social Value Update:**


The volunteering community project for Waterside Day Centre is now complete.





What it looked like before...

The mini project was completed over a two-week period by the volunteers.

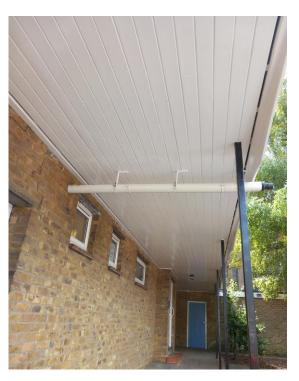



And what it looks like now...









Centre Manger, Jenny Edwards extended appreciation on behalf of the Centre and the families they support in a letter to the Jackson team. She wrote, "We are so grateful to you for organising this project and to the team for their hard work. The staff were very considerate of our work and completed the project without any disruption to our service which was fantastic. The canopy is looking so much better; it is brighter, cleaner, and more welcoming for staff, families, and visitors to the centre."





Jackson Public Liaison Officer, Juliet (in front) with Jenny and Stuart.

As the works progress, we remain committed to the safety of pedestrians and the general public, and we welcome you to contact us if you have queries or concerns by sending an email to

<u>BathStreet@jackson-civils.co.uk</u> or calling **07811941681**.

