

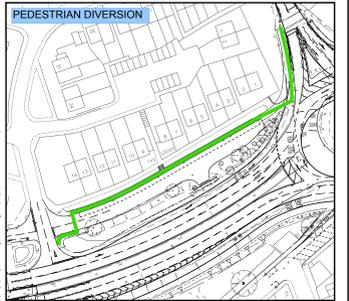
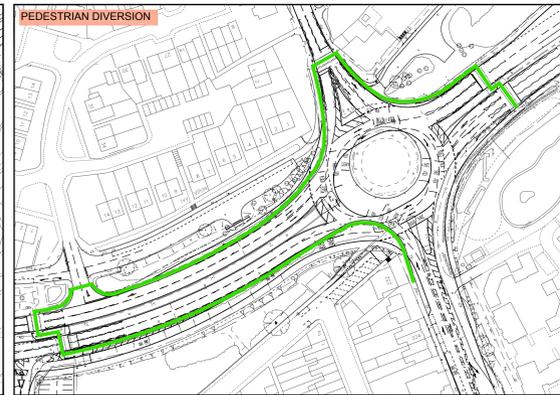
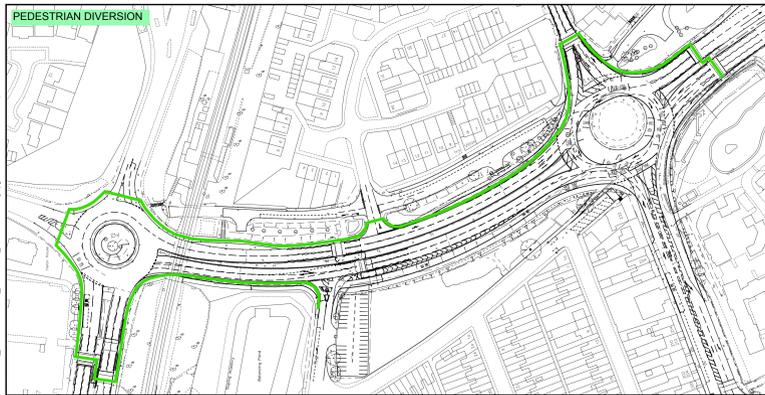



# ST CLEMENTS WAY, GREENHITHE IMPROVEMENT SCHEME

~ INDICATIVE SEQUENCE OF WORKS ~

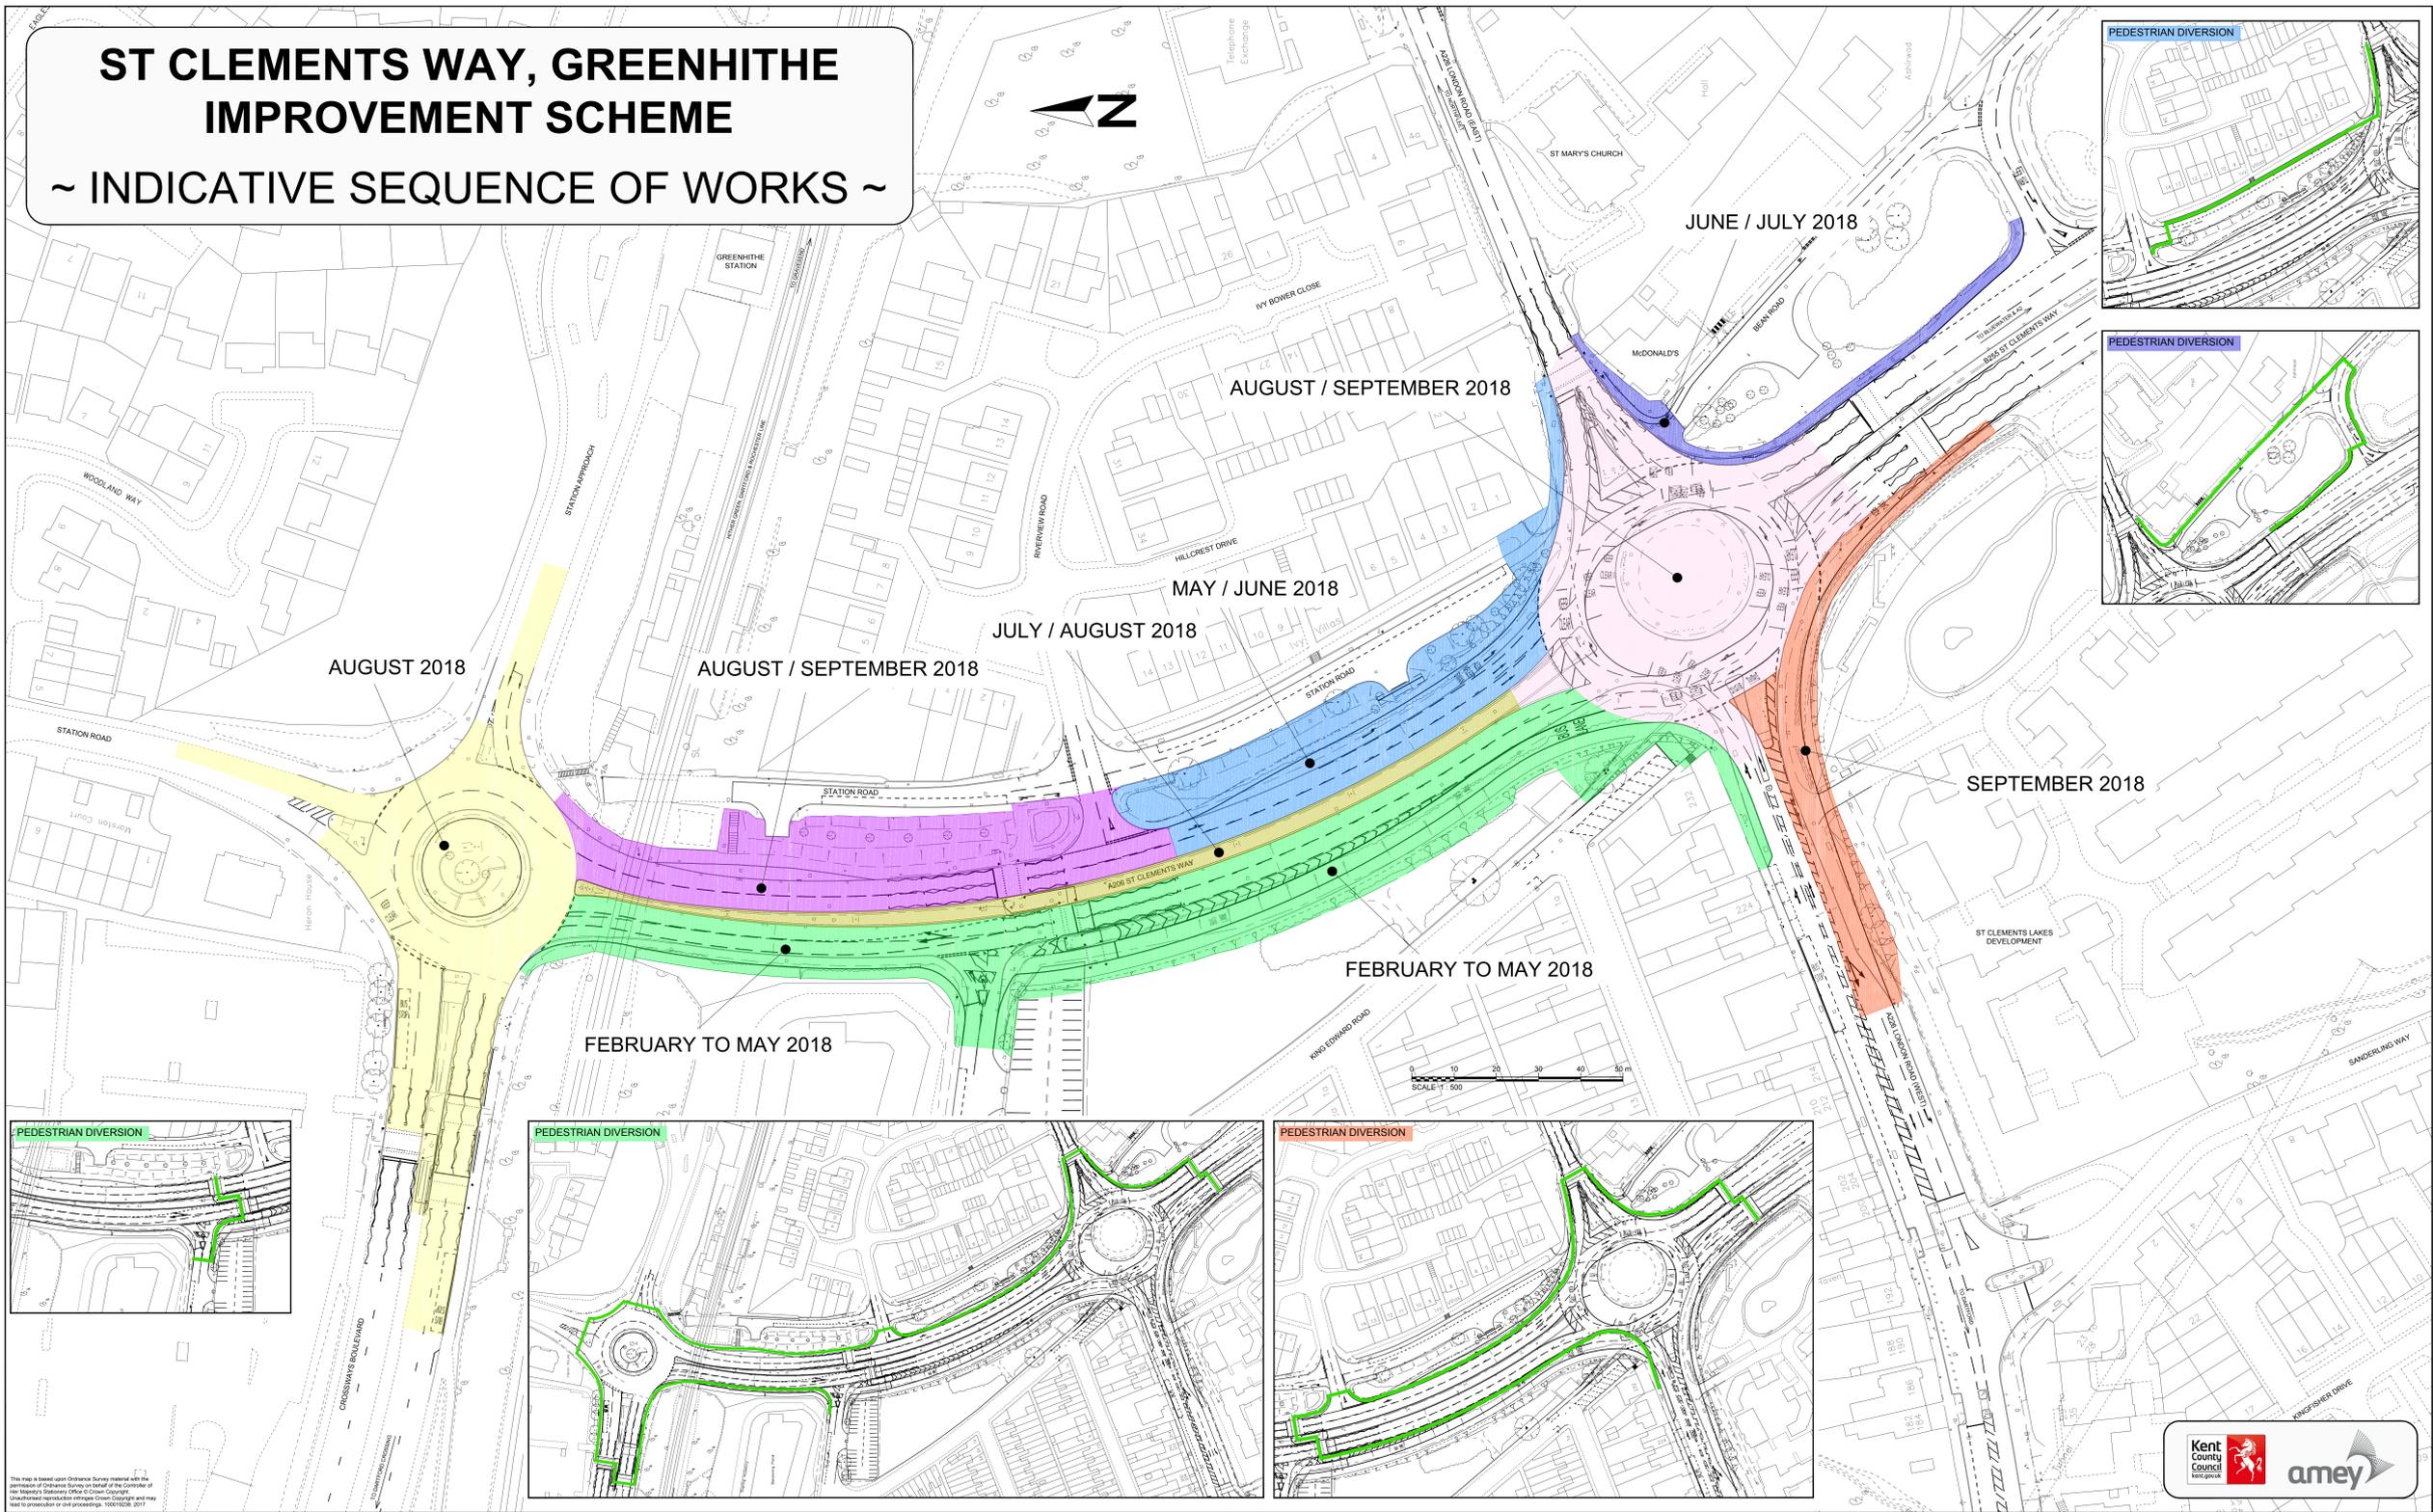

## INDICATIVE CONSTRUCTION TIME-LINE

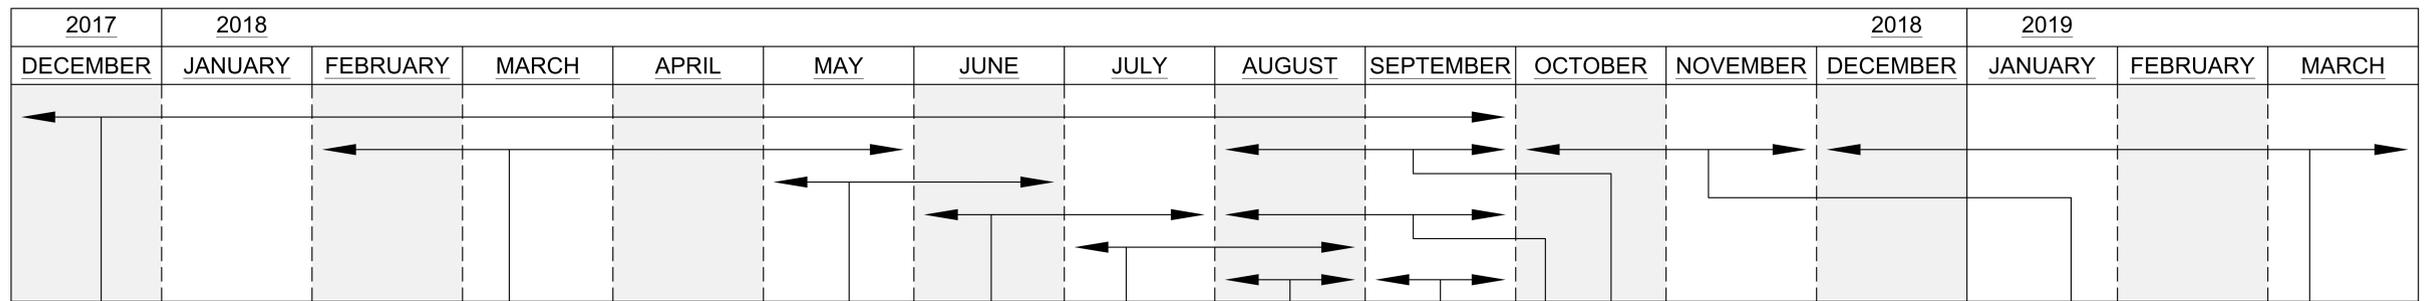

**DECEMBER 2017 TO SEPTEMBER 2018**

- Site Clearance throughout site.
- Utility diversions throughout site.

**MAY / JUNE 2018**

- Widening between Riverview Road and London Road (East).
- Footway/cycleway to Mounts Road.
- Off-peak lane closures.

**AUGUST 2018**

- Crossways Boulevard and roundabout.
- Off-peak lane closures.
- Overnight closures Station Road & Station Approach.

**AUGUST / SEPTEMBER 2018**

- St Clements Way roundabout & approaches.
- Overnight closures London Road (East).

**AUGUST / SEPTEMBER 2018**

- St Clements Way from Crossways Boulevard to Riverview Road

**OCTOBER / NOVEMBER 2018**

- Final surfacing throughout site.
- Off-peak lane closures.

**FEBRUARY TO MAY 2018**

- Bus lane and widening between London Road & Steele Avenue.
- Widening between Steele Avenue & Crossways Boulevard.
- Off-peak lane closures.

**JUNE / JULY 2018**

- London Road (East) & McDonalds area

**JULY / AUGUST 2018**

- St Clements Way central reserve
- Off-peak lane closures

**SEPTEMBER 2018**

- London Road (West) & St Clements Lakes area.

**2019**

- General finishing works.
- Landscape planting works.
- Off-peak lane closures

**NOTE:**

- Anticipated timings and locations shown are indicative and may change as construction progresses. Actual timings will be dependant on or influenced by factors such as weather or site conditions.
